


		Name	Duration	Start	Finish	Predecessors	Resource Names
1		Project Initiation	4 days	18/05/26, 8:00am	21/05/26, 5:00pm		
2		Project Topic Finalization	1 day	18/05/26, 8:00am	18/05/26, 5:00pm		Project Manager
3		Requirement Gathering	2 days	19/05/26, 8:00am	20/05/26, 5:00pm	2	Project Manager
4		BRD Review	1 day	21/05/26, 8:00am	21/05/26, 5:00pm	3	Project Manager
5		Initiation Milestone	0 days	21/05/26, 5:00pm	21/05/26, 5:00pm	4	Project Manager
6		Requirement Analysis	7 days	22/05/26, 8:00am	01/06/26, 5:00pm		
7		Prepare SRS Document	3 days	22/05/26, 8:00am	26/05/26, 5:00pm	5	Project Manager
8		Functional Requirement An...	2 days	27/05/26, 8:00am	28/05/26, 5:00pm	7	Project Manager
9		Non-Functional Requireme...	1 day	29/05/26, 8:00am	29/05/26, 5:00pm	8	Project Manager
10		Requirement Traceability M...	1 day	01/06/26, 8:00am	01/06/26, 5:00pm	9	Project Manager
11		Requirement Analysis Milest...	0 days	01/06/26, 5:00pm	01/06/26, 5:00pm	10	Project Manager
12		System Design	10 days	02/06/26, 8:00am	15/06/26, 5:00pm		
13		Use Case Diagram	1 day	02/06/26, 8:00am	02/06/26, 5:00pm	11	UI/UX Designer
14		DFD Level 0	1 day	03/06/26, 8:00am	03/06/26, 5:00pm	13	UI/UX Designer
15		DFD Level 1	1 day	04/06/26, 8:00am	04/06/26, 5:00pm	14	UI/UX Designer
16		ER Diagram	1 day	05/06/26, 8:00am	05/06/26, 5:00pm	15	Database Engineer
17		Class Diagram	1 day	08/06/26, 8:00am	08/06/26, 5:00pm	16	UI/UX Designer
18		Sequence Diagram	1 day	09/06/26, 8:00am	09/06/26, 5:00pm	17	UI/UX Designer
19		Activity Diagram	1 day	10/06/26, 8:00am	10/06/26, 5:00pm	18	UI/UX Designer
20		State Diagram	1 day	11/06/26, 8:00am	11/06/26, 5:00pm	19	UI/UX Designer
21		Architecture Design	1 day	12/06/26, 8:00am	12/06/26, 5:00pm	20	Project Manager
22		UI/UX Finalization	1 day	15/06/26, 8:00am	15/06/26, 5:00pm	21	UI/UX Designer
23		Design Milestone	0 days	15/06/26, 5:00pm	15/06/26, 5:00pm	22	Project Manager
24		Database Design	5 days	16/06/26, 8:00am	22/06/26, 5:00pm		
25		Database Schema Design	2 days	16/06/26, 8:00am	17/06/26, 5:00pm	23	Database Engineer
26		Table Relationship Design	1 day	18/06/26, 8:00am	18/06/26, 5:00pm	25	Database Engineer
27		Constraints & Indexing	1 day	19/06/26, 8:00am	19/06/26, 5:00pm	26	Database Engineer
28		PostgreSQL Setup	1 day	22/06/26, 8:00am	22/06/26, 5:00pm	27	Database Engineer
29		Database Milestone	0 days	22/06/26, 5:00pm	22/06/26, 5:00pm	28	Database Engineer
30		Frontend Development	11 days	23/06/26, 8:00am	07/07/26, 5:00pm		
31		React + Vite Setup	1 day	23/06/26, 8:00am	23/06/26, 5:00pm	29	Frontend Developer
32		Tailwind CSS Setup	1 day	24/06/26, 8:00am	24/06/26, 5:00pm	31	Frontend Developer
33		Authentication UI	2 days	25/06/26, 8:00am	26/06/26, 5:00pm	32	Frontend Developer
34		Dashboard UI	2 days	29/06/26, 8:00am	30/06/26, 5:00pm	33	Frontend Developer
35		Group Management UI	1 day	01/07/26, 8:00am	01/07/26, 5:00pm	34	Frontend Developer



[illegible]

		Name	Duration	Start	Finish	Predecessors	Resource Names
36		Map View UI	2 days	02/07/26, 8:00am	03/07/26, 5:00pm	35	Frontend Developer
37		Settings UI	1 day	06/07/26, 8:00am	06/07/26, 5:00pm	36	Frontend Developer
38		Accessibility Features UI	1 day	07/07/26, 8:00am	07/07/26, 5:00pm	37	Frontend Developer
39		Frontend Milestone	0 days	07/07/26, 5:00pm	07/07/26, 5:00pm	38	Frontend Developer
40		Backend Development	11 days	08/07/26, 8:00am	22/07/26, 5:00pm		
41		Node.js + Express Setup	1 day	08/07/26, 8:00am	08/07/26, 5:00pm	39	Backend Developer
42		Authentication APIs	2 days	09/07/26, 8:00am	10/07/26, 5:00pm	41	Backend Developer
43		User Management APIs	1 day	13/07/26, 8:00am	13/07/26, 5:00pm	42	Backend Developer
44		Group APIs	2 days	14/07/26, 8:00am	15/07/26, 5:00pm	43	Backend Developer
45		Role & Permission Logic	1 day	16/07/26, 8:00am	16/07/26, 5:00pm	44	Backend Developer
46		Location APIs	2 days	17/07/26, 8:00am	20/07/26, 5:00pm	45	Backend Developer
47		Socket.io Integration	1 day	21/07/26, 8:00am	21/07/26, 5:00pm	46	Backend Developer
48		Notification APIs	1 day	22/07/26, 8:00am	22/07/26, 5:00pm	47	Backend Developer
49		Backend Milestone	0 days	22/07/26, 5:00pm	22/07/26, 5:00pm	48	Backend Developer
50		Testing & Deployment	4 days	23/07/26, 8:00am	28/07/26, 5:00pm		
51		Unit Testing	1 day	23/07/26, 8:00am	23/07/26, 5:00pm	49	QA Tester
52		Integration Testing	1 day	24/07/26, 8:00am	24/07/26, 5:00pm	51	QA Tester
53		Bug Fixing	1 day	27/07/26, 8:00am	27/07/26, 5:00pm	52	QA Tester
54		Deployment	1 day	28/07/26, 8:00am	28/07/26, 5:00pm	53	DevOps Engineer
55		Final Project Milestone	0 days	28/07/26, 5:00pm	28/07/26, 5:00pm	54	Project Manager

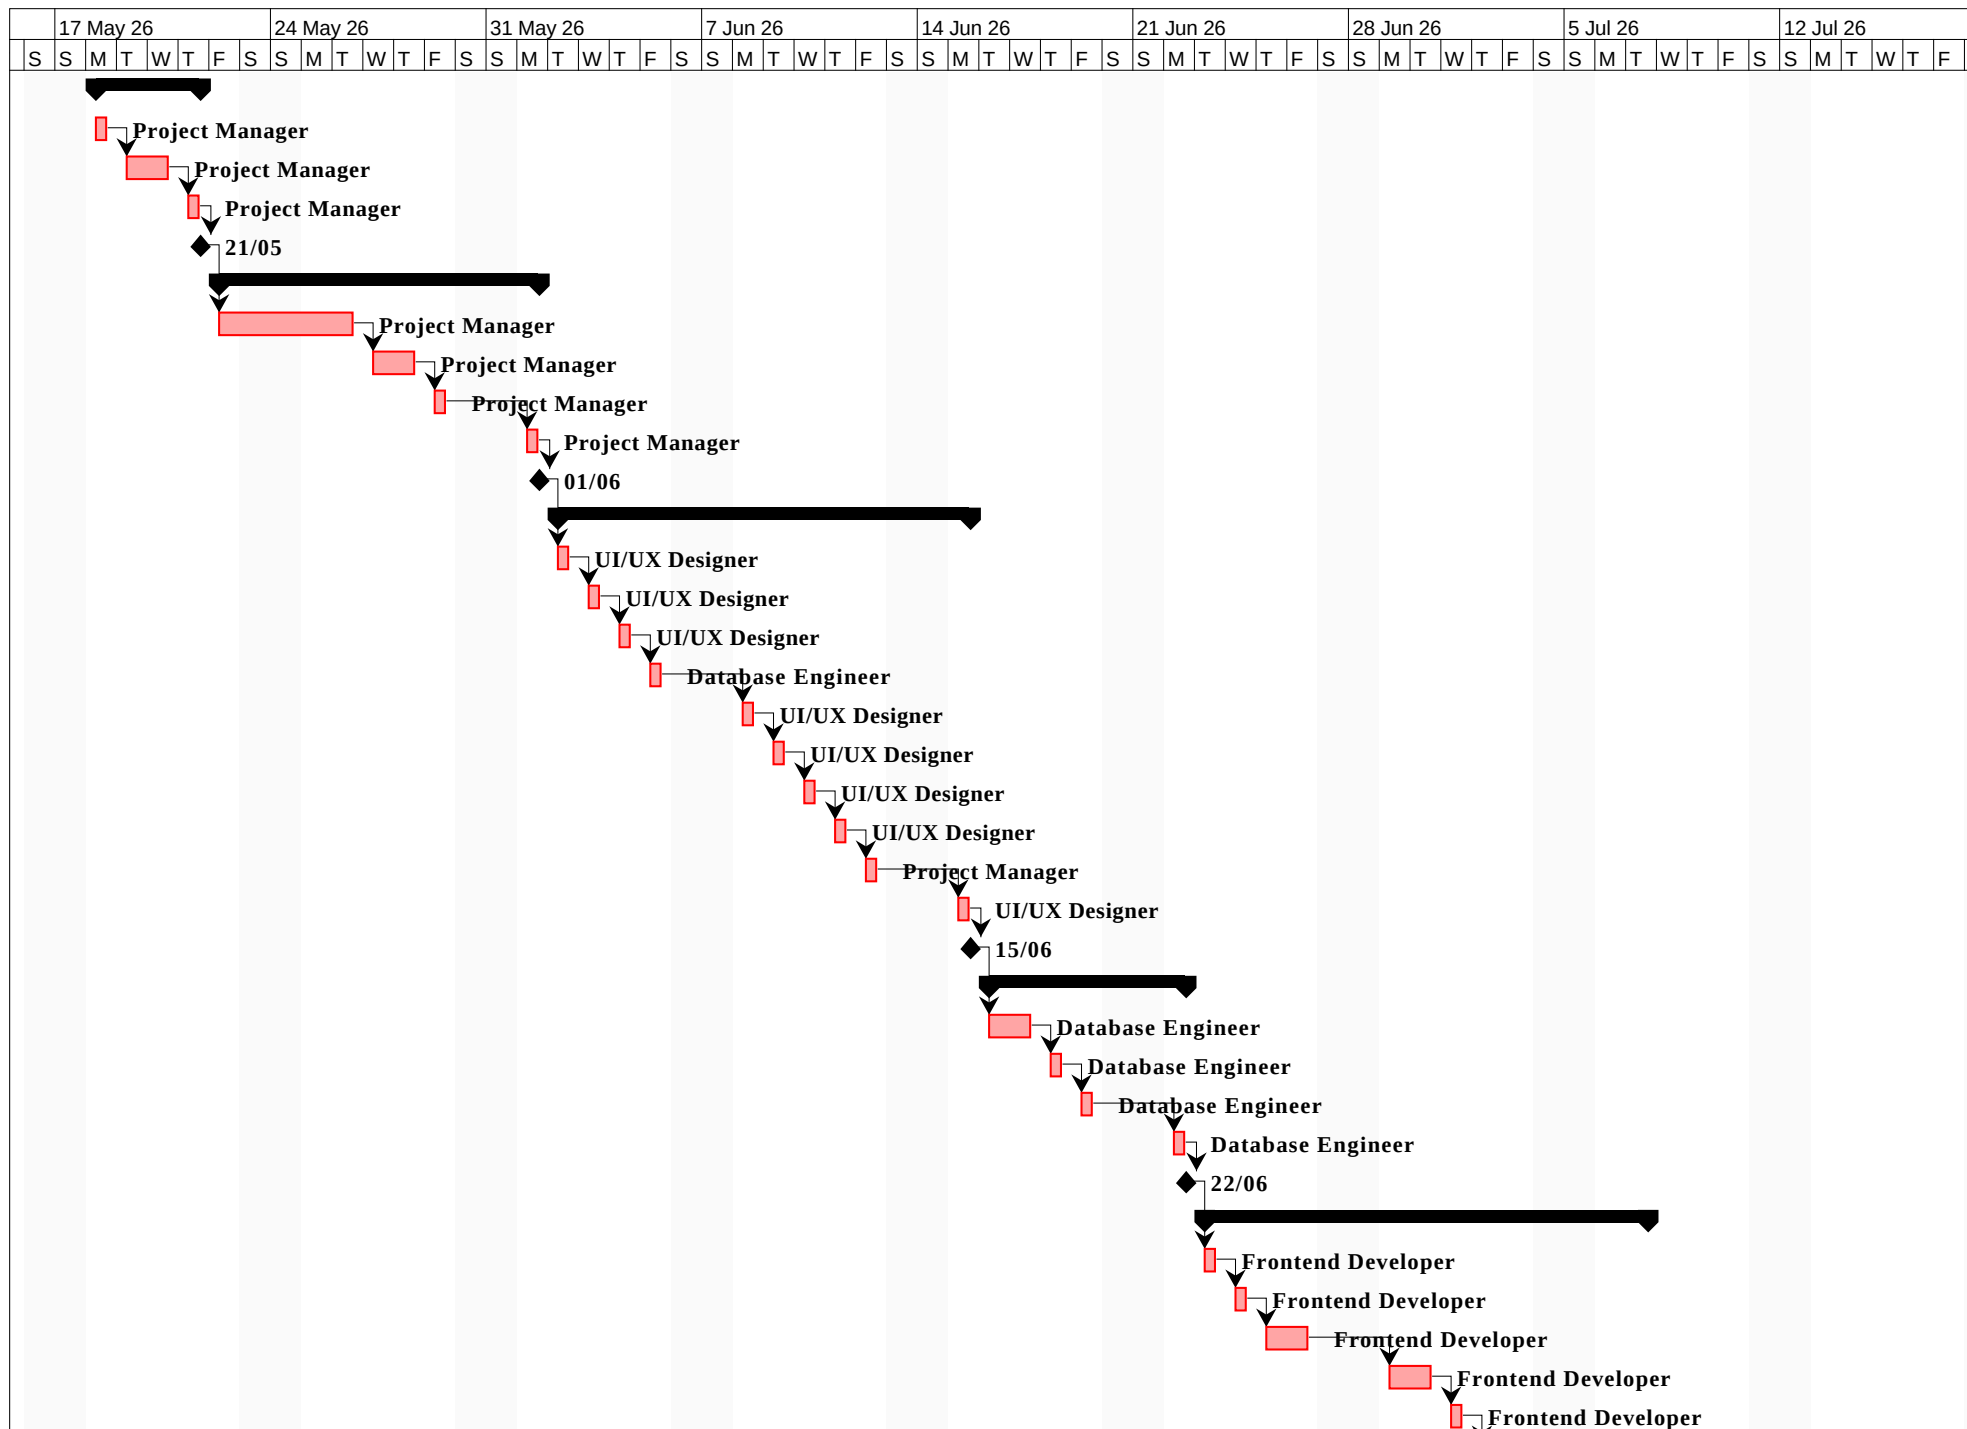
