


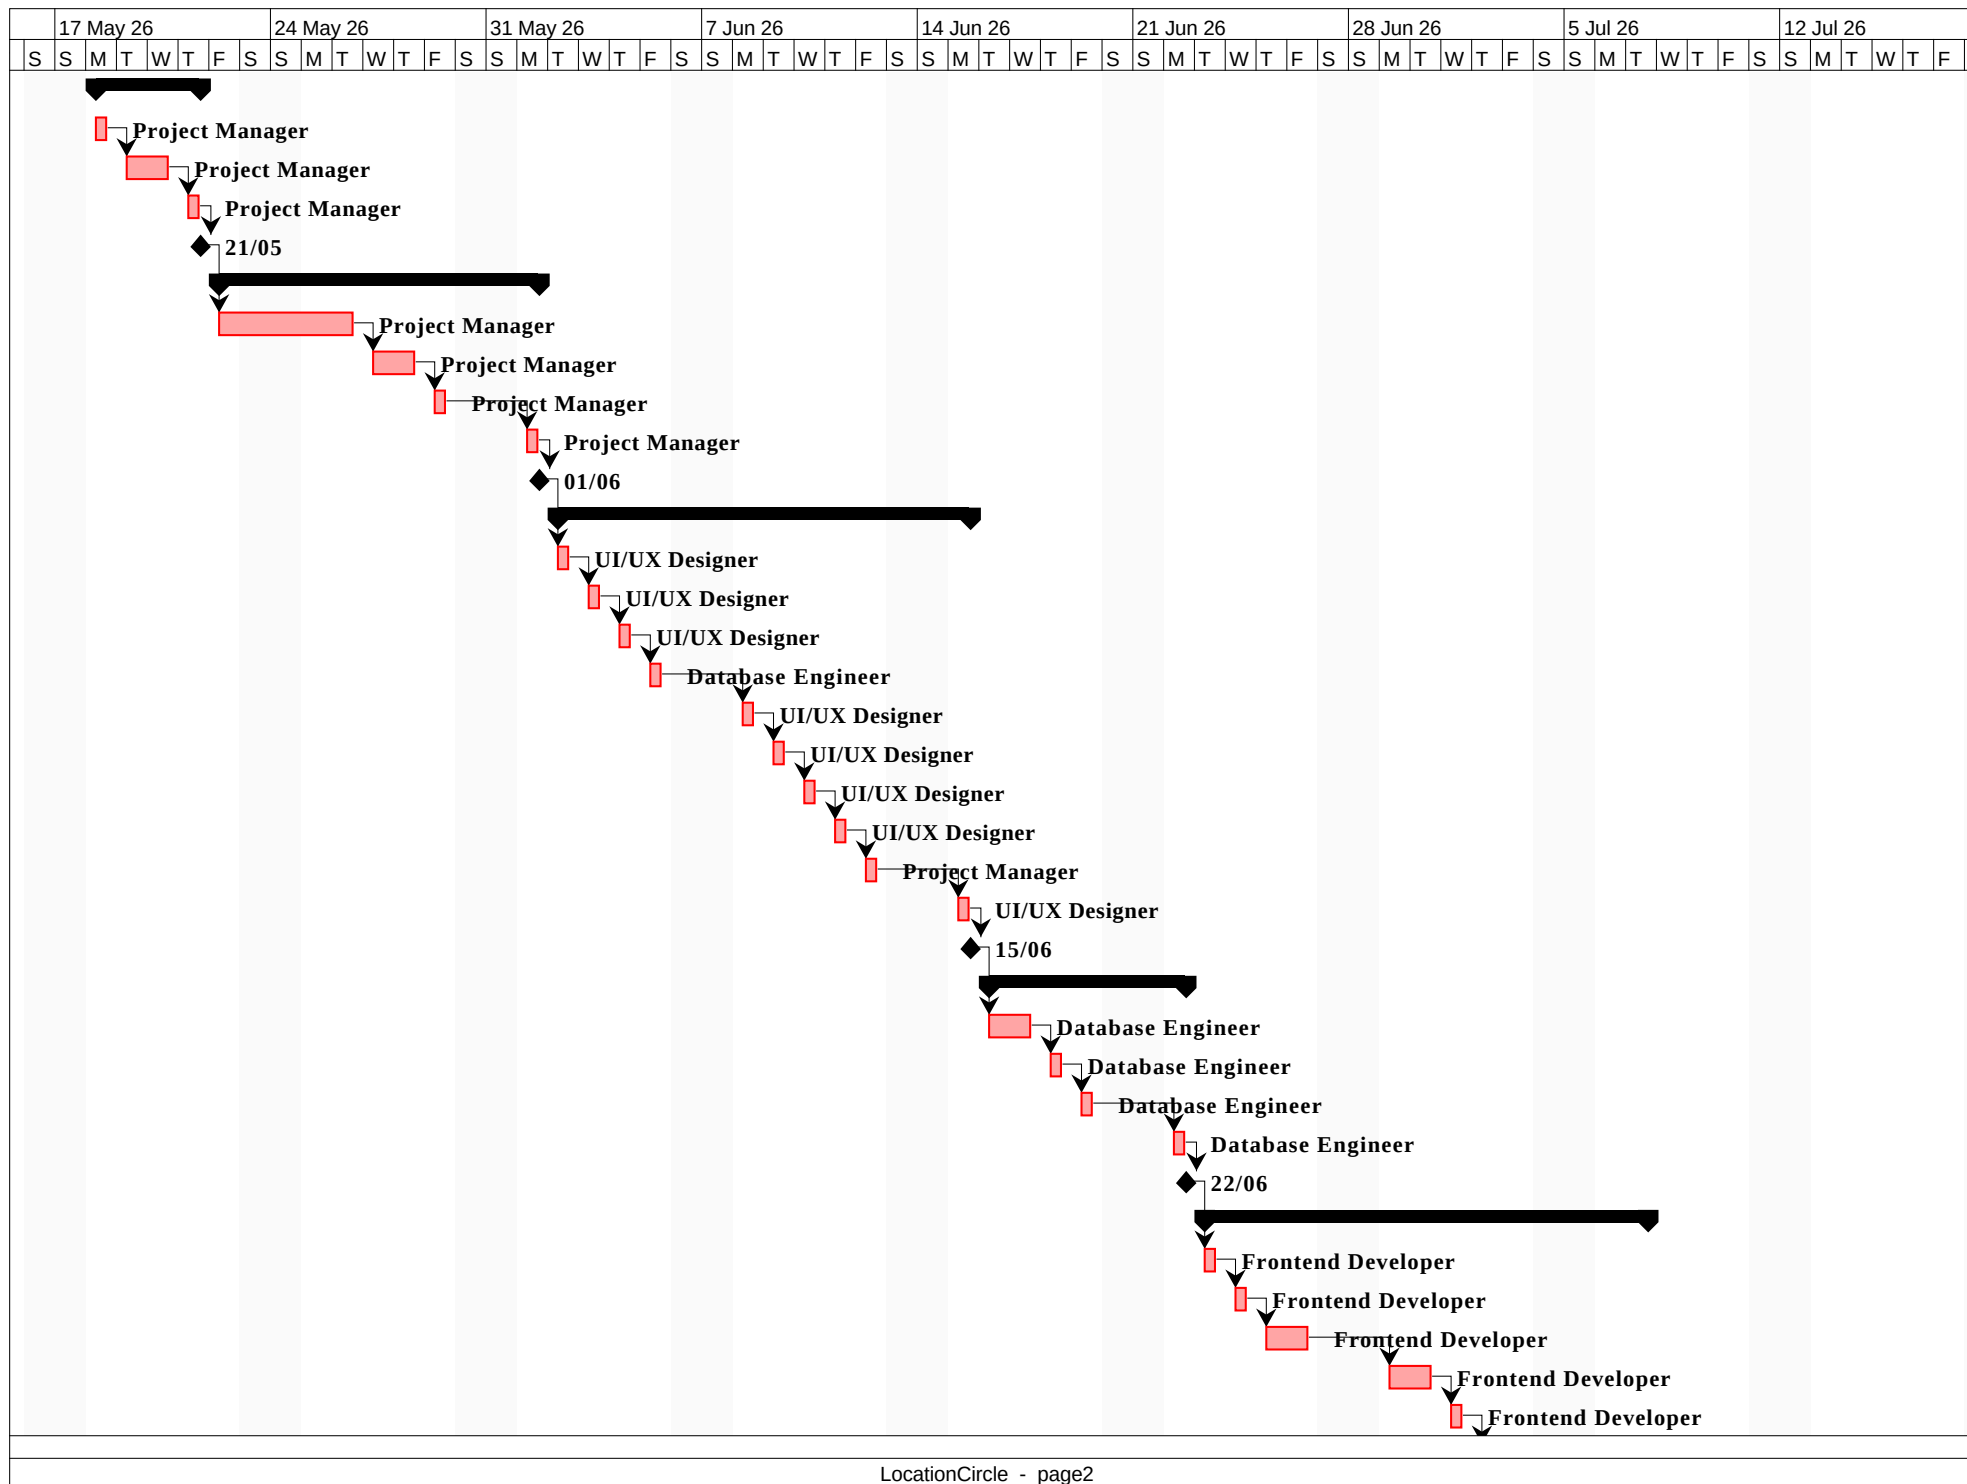

19 Jul 26							26 Jul 26							2 Aug 26							9 Aug 26							16 Aug 26							23 Aug 26						
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	

LocationCircle - page3

		Name	Duration	Start	Finish	Predecessors	Resource Names
36		Map View UI	2 days	02/07/26, 8:00am	03/07/26, 5:00pm	35	Frontend Developer
37		Settings UI	1 day	06/07/26, 8:00am	06/07/26, 5:00pm	36	Frontend Developer
38		Accessibility Features UI	1 day	07/07/26, 8:00am	07/07/26, 5:00pm	37	Frontend Developer
39		Frontend Milestone	0 days	07/07/26, 5:00pm	07/07/26, 5:00pm	38	Frontend Developer
40		Backend Development	11 days	08/07/26, 8:00am	22/07/26, 5:00pm		
41		Node.js + Express Setup	1 day	08/07/26, 8:00am	08/07/26, 5:00pm	39	Backend Developer
42		Authentication APIs	2 days	09/07/26, 8:00am	10/07/26, 5:00pm	41	Backend Developer
43		User Management APIs	1 day	13/07/26, 8:00am	13/07/26, 5:00pm	42	Backend Developer
44		Group APIs	2 days	14/07/26, 8:00am	15/07/26, 5:00pm	43	Backend Developer
45		Role & Permission Logic	1 day	16/07/26, 8:00am	16/07/26, 5:00pm	44	Backend Developer
46		Location APIs	2 days	17/07/26, 8:00am	20/07/26, 5:00pm	45	Backend Developer
47		Socket.io Integration	1 day	21/07/26, 8:00am	21/07/26, 5:00pm	46	Backend Developer
48		Notification APIs	1 day	22/07/26, 8:00am	22/07/26, 5:00pm	47	Backend Developer
49		Backend Milestone	0 days	22/07/26, 5:00pm	22/07/26, 5:00pm	48	Backend Developer
50		Testing & Deployment	4 days	23/07/26, 8:00am	28/07/26, 5:00pm		
51		Unit Testing	1 day	23/07/26, 8:00am	23/07/26, 5:00pm	49	QA Tester
52		Integration Testing	1 day	24/07/26, 8:00am	24/07/26, 5:00pm	51	QA Tester
53		Bug Fixing	1 day	27/07/26, 8:00am	27/07/26, 5:00pm	52	QA Tester
54		Deployment	1 day	28/07/26, 8:00am	28/07/26, 5:00pm	53	DevOps Engineer
55		Final Project Milestone	0 days	28/07/26, 5:00pm	28/07/26, 5:00pm	54	Project Manager

Project Initiation
Duration 4 days
Start 18/05/26, 8:00am
Finish 21/05/26, 5:00pm

Project Topic Finalization
Duration 1 day
Start 18/05/26, 8:00am
Finish 18/05/26, 5:00pm

Requirement Gathering
Duration 2 days
Start 19/05/26, 8:00am
Finish 20/05/26, 5:00pm

BRD Review
Duration 1 day
Start 21/05/26, 8:00am
Finish 21/05/26, 5:00pm



Requirement Analysis
Duration 7 days
Start 22/05/26, 8:00am
Finish 01/06/26, 5:00pm


System Design
Duration 10 days
Start 02/06/26, 8:00am
Finish 15/06/26, 5:00pm

Database Design
Duration 5 days
Start 16/06/26, 8:00am
Finish 22/06/26, 5:00pm

Frontend Development
Duration 11 days
Start 23/06/26, 8:00am
Finish 07/07/26, 5:00pm

Backend Development
Duration 11 days
Start 08/07/26, 8:00am
Finish 22/07/26, 5:00pm

Testing & Deployment
Duration 4 days
Start 23/07/26, 8:00am
Finish 28/07/26, 5:00pm

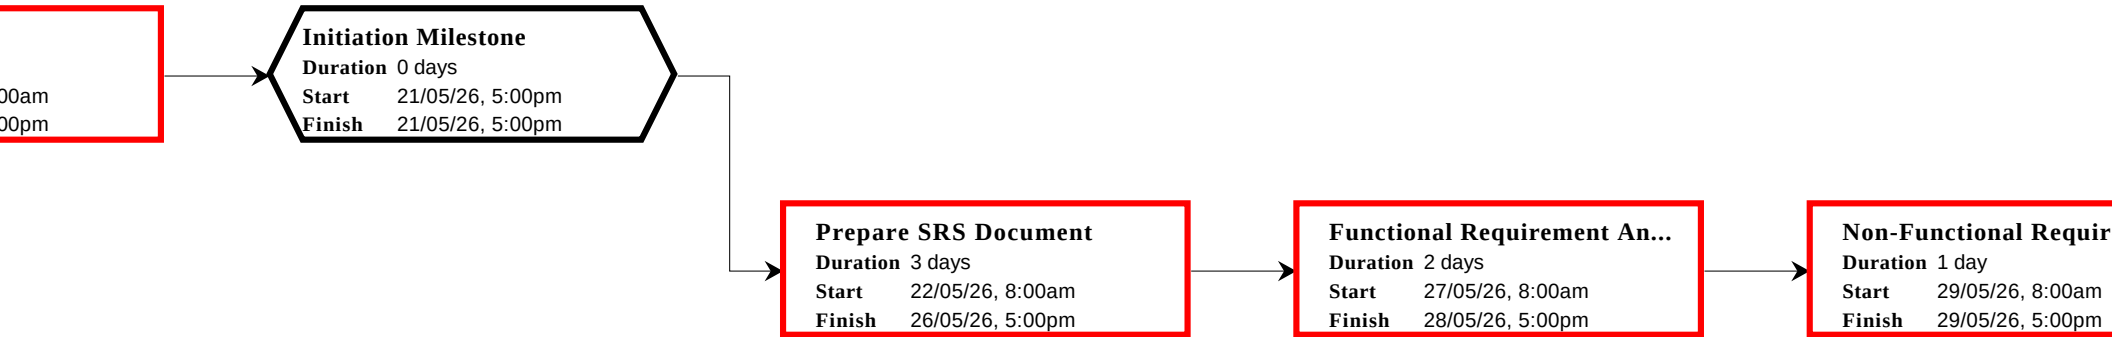

Additional Requirements
Duration 1 day
Start 01/05/26, 8:00am
Finish 01/05/26, 5:00pm

Requirement Traceability Matrix
Duration 1 day
Start 01/06/26, 8:00am
Finish 01/06/26, 5:00pm

Requirement Analysis Milestones
Duration 0 days
Start 01/06/26, 5:00pm
Finish 01/06/26, 5:00pm

Use Case Diagram
Duration 1 day
Start 02/06/26, 8:00am
Finish 02/06/26, 5:00pm

DFD Level 0
Duration 1 day
Start 03/06/26, 8:00am
Finish 03/06/26, 5:00pm

FD Level 0
Duration 1 day
Start 03/06/26, 8:00am
Finish 03/06/26, 5:00pm



DFD Level 1
Duration 1 day
Start 04/06/26, 8:00am
Finish 04/06/26, 5:00pm




ER Diagram
Duration 1 day
Start 05/06/26, 8:00am
Finish 05/06/26, 5:00pm





Class Diagram
Duration 1 day
Start 08/06/26, 8:00am
Finish 08/06/26, 5:00pm





Sequence Diagram
Duration 1 day
Start 08/06/26, 8:00am
Finish 08/06/26, 5:00pm








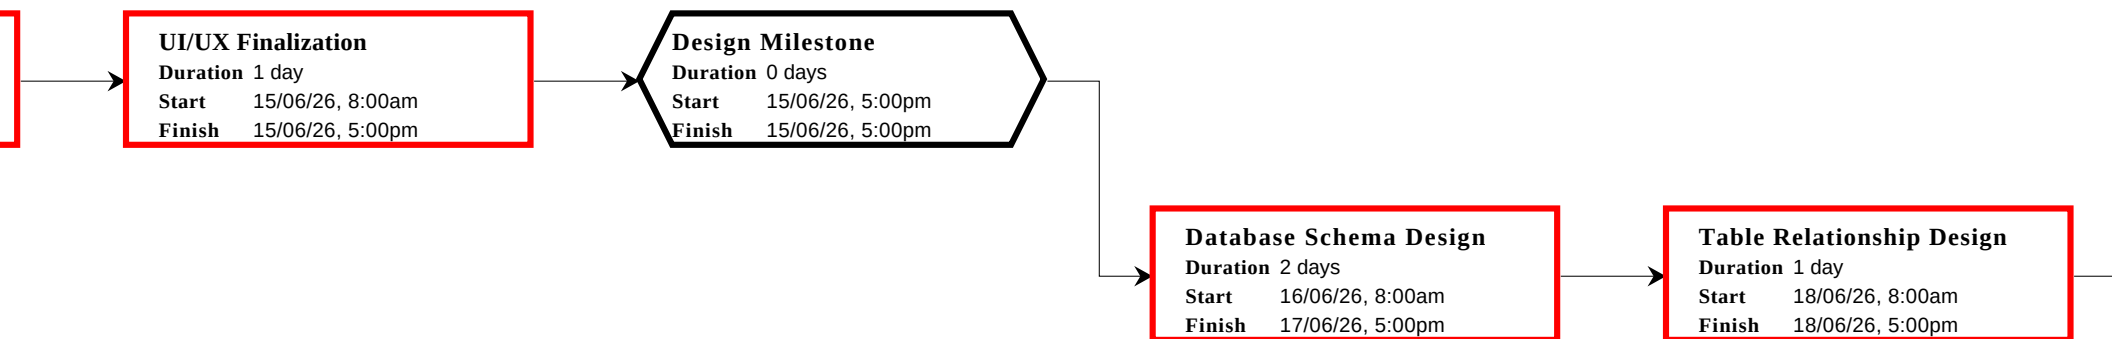


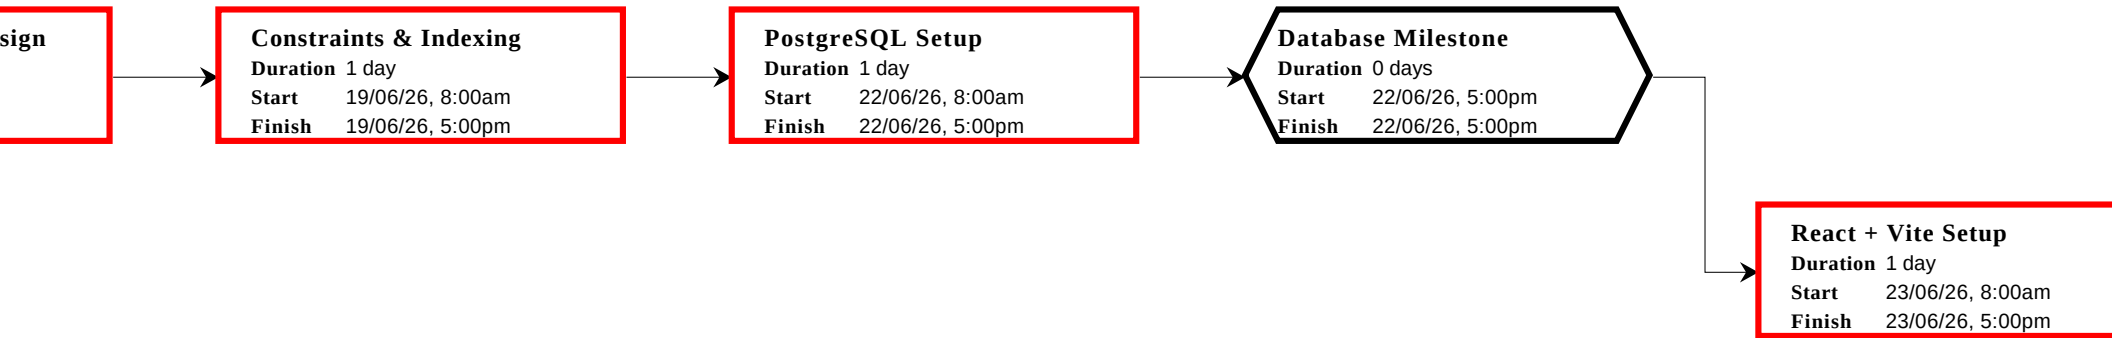














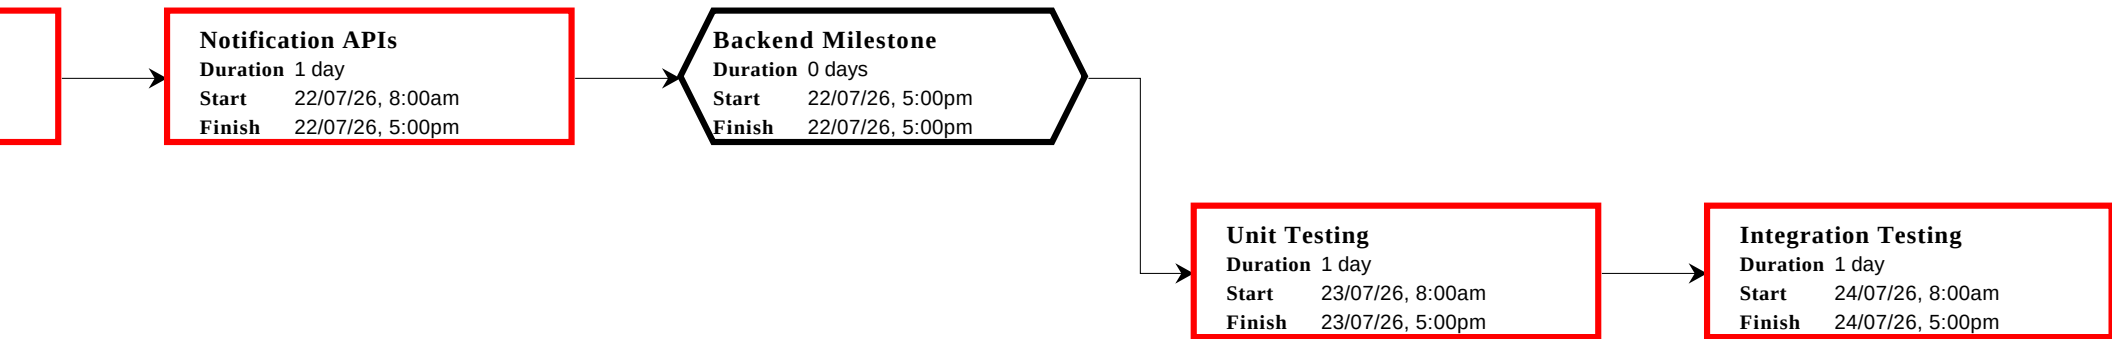





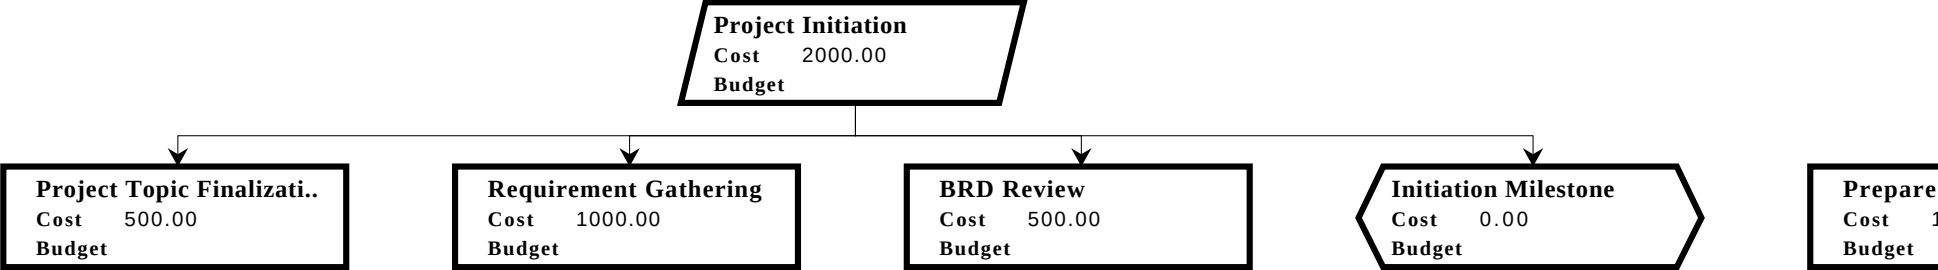

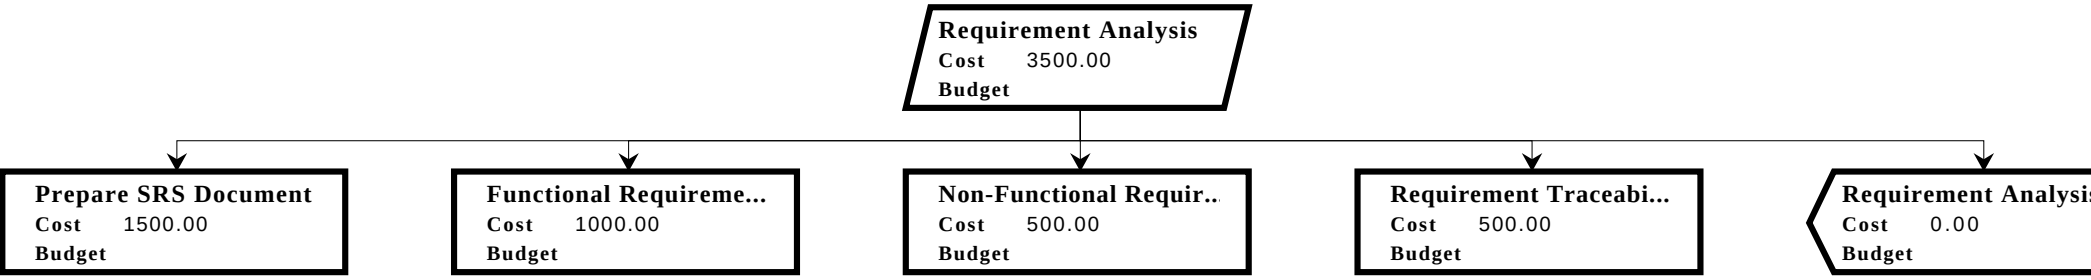



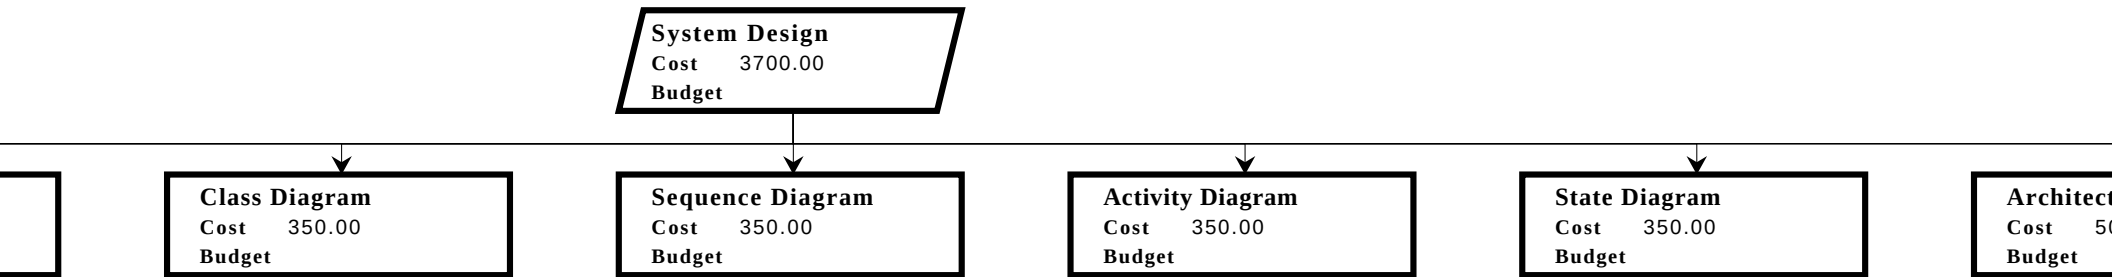



Architecture Design

Cost 500.00

Budget

UI/UX Finalization

Cost 350.00

Budget

Design Milestone

Cost 0.00

Budget

Database Schema De...


Cost 800.00


Budget


Table Relationship De...


Cost 400.00


Budget

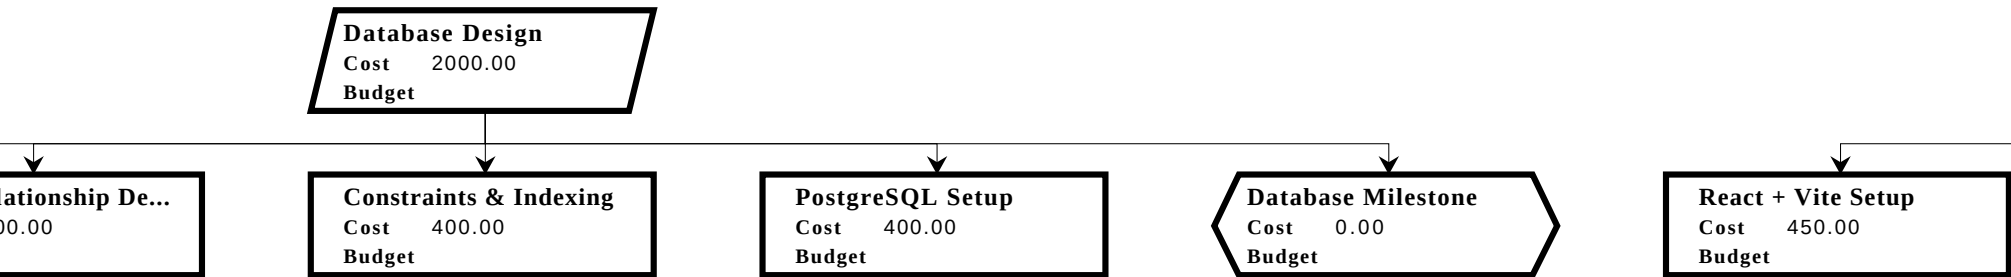


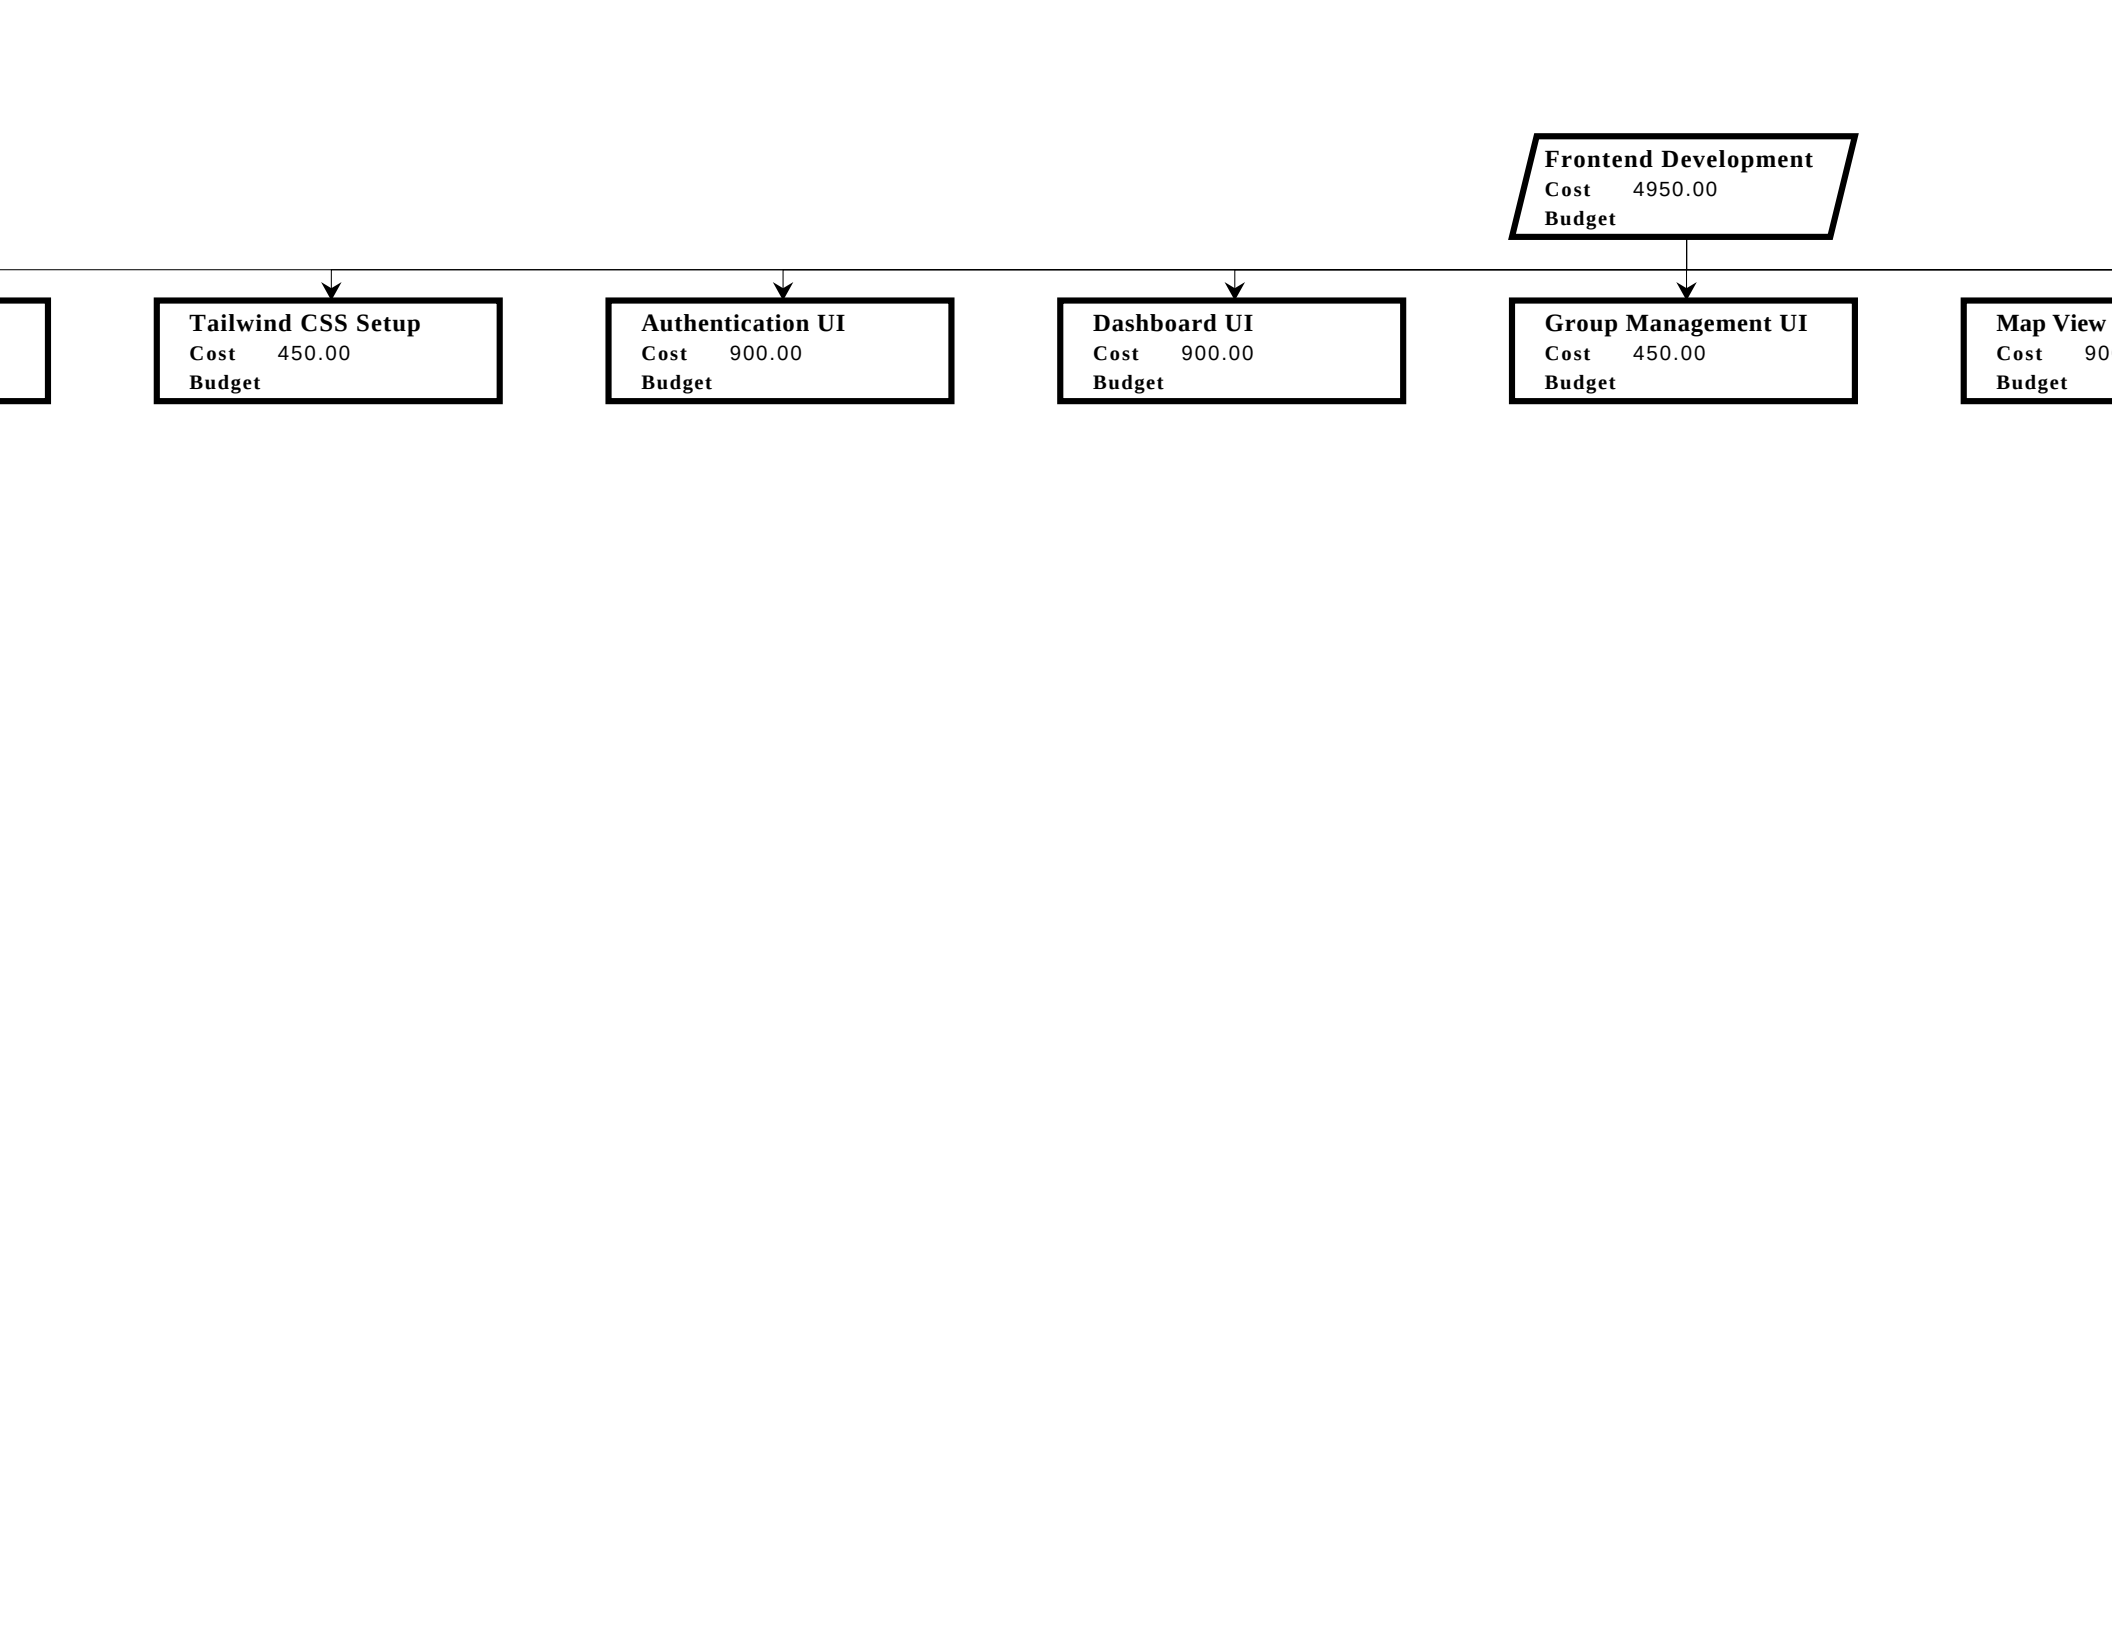



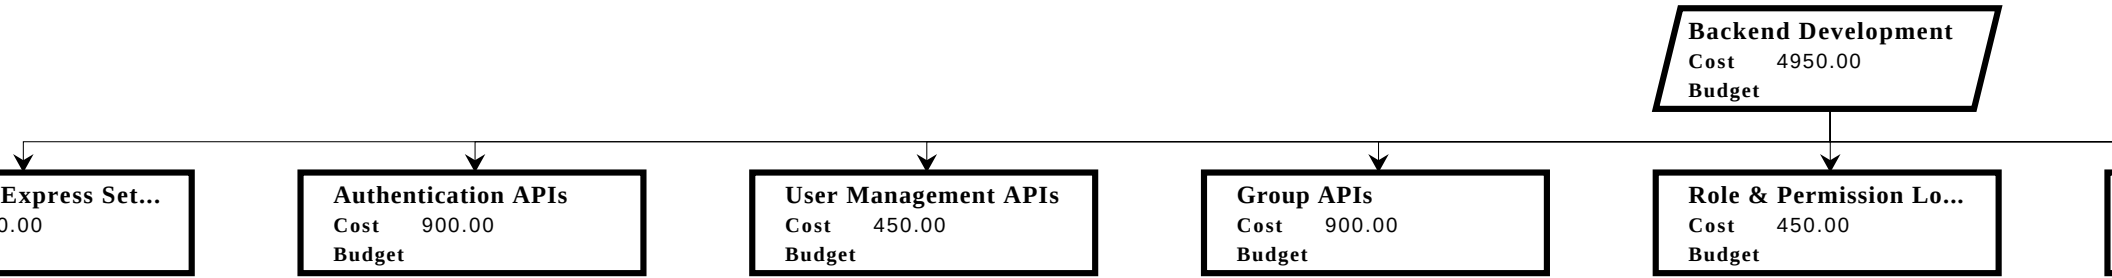



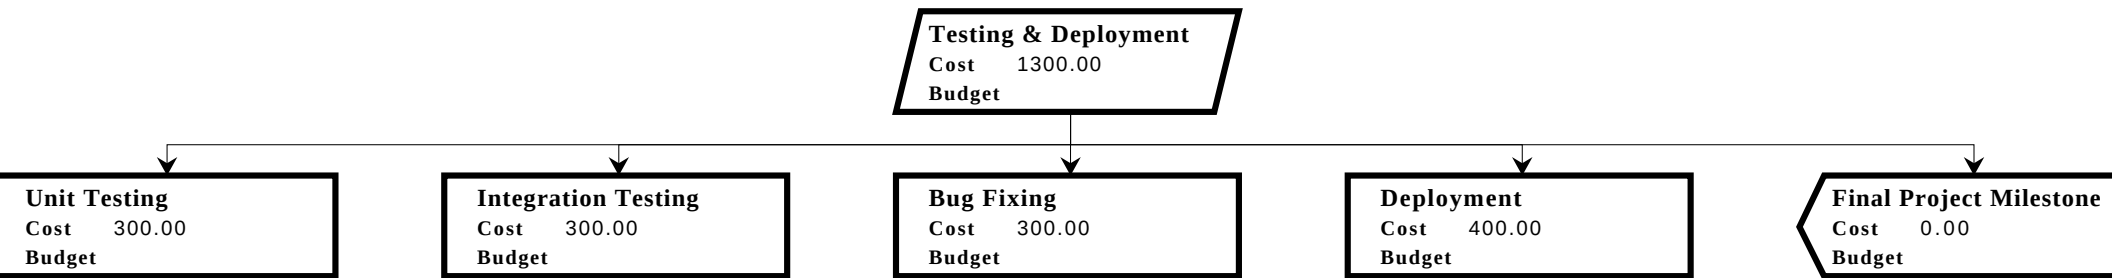



Project Milestone

0

		Name	RBS	Type	E-mail Address	Material Label
1		Project Manager		Work		
2		Frontend Developer		Work		
3		Backend Developer		Work		
4		Database Engineer		Work		
5		UI/UX Designer		Work		
6		QA Tester		Work		
7		DevOps Engineer		Work		

Accrue At	Base Calendar
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
Prorated	Standard
LocationCircle - page3	

Project Manager	
Cost	6000.00
Budget	0.00

Frontend Developer	
Cost	4950.00
Budget	0.00

Backend Developer	
Cost	4950.00
Budget	0.00

Database Engineer	
Cost	2400.00
Budget	0.00

UI/UX Designer	
Cost	2400.00
Budget	0.00

UI/UX Designer

Cost 2800.00

Budget 0.00

QA Tester

Cost 900.00

Budget 0.00

DevOps Engineer

Cost 400.00

Budget 0.00
